SARAS Development Review and Client Feedback

Module: CET257 Enterprise Project
Team: Team 9 — SARAS Labs
Members: Rijan Kapur Poudel and Sushank Jung Rawal
Purpose: Connect later development to the original plan and recorded client priorities.

At Week 7, we could show one Fire Safety learner journey. The later work asked more of us: explain what completion meant, connect a learner's result to the responsible trainer and give the 3D activities a clear learning purpose. **Separating lessons, assessments and practice records** was our strongest response to the client's feedback.

Some parts are still incomplete, including the spill and isolation decisions, trainer account-creation authority and recovery after leaving an unsaved task. This review follows the changes, the work behind them and what we still need to resolve.

1 Starting point and client direction

The Week 7 demonstration focused on one Fire Safety journey. Mr. Ninson Lama's written reply on 1 September 2026 found that route understandable and valued active hazard recognition and explanatory feedback. His next priorities were clearer progress and completion information and more consistent feedback. He also repeated that digital completion should remain separate from practical competence, and that learner development should take priority before broader features.

2 Changes connected to recorded feedback

Table 1 Recorded feedback and development responses

Recorded priority	Later response	Effect and remaining check
Explain progress and what remains	Current-curriculum progress calculations, distinct activity/test/practice records and clearer readiness information	Avoids inflated totals and ambiguous completion; learner understanding still needs observation
Make feedback consistent	Clearer lesson instructions, persistent test responses, authorised review and separate recovery states	Connects the learner response with its explanation; content review remains necessary
Keep the learner route dependable	Stale-response protection, stable practice retry identities, session recovery and phone interaction refinements	Supports recovery within the open page; retry consistency and recovery after leaving require selected-environment checks
Keep digital and practical competence separate	Practice does not issue certificates or add XP; chapter passes remain distinct from course certification	Protects the meaning of results; workplace content must receive qualified review
Administrative functions may be useful later	Trainer assignment, account management, records and analytics	Later scope extends the application; the correspondence does not constitute detailed approval of every management feature

The later September replies turn these priorities into specific task, supervision and recovery requirements. Table 2 compares each request with the delivered response, including the unresolved trainer-provisioning permission. Support for a task area or assigned supervision does not establish approval of every procedure or account operation.

Before-and-after evaluation of the requested changes

The later correspondence makes the requirements more specific than a general request for a better interface. The following comparisons examine whether the implemented response addresses the actual question. They evaluate retained source and correspondence, not an unrecorded client acceptance session.

Table 2 Client requests compared with delivered design and remaining gaps

Dated request and initial problem	Current design response	Evaluation and remaining action
7 September: one overall progress figure could not distinguish reading, passed questions and full module completion	Separate lesson progress, assessment attempts, formative practice and certificate information	Stronger than relabelling one percentage because outcome types remain distinct in records. Independent interpretation is still unmeasured.
7 September: start with hazard recognition or spill response, identifying the substance and appropriate personal protective equipment (PPE)	Guided hazard and spill spaces; spill steps collect a kit, place barriers and apply absorbent	The task area is relevant, but the spill configuration has no explicit substance-identification or PPE decision. Those client points are not fully implemented. Procedure review and a revised task definition are needed before operational use.
14 September: identify incomplete learning and difficulty within assigned personnel; reserve broader administration	Assigned learner records, category tabs and scoped analytics; trainers can also create assigned learners	The practice summary exposes completion and retries, not every saved choice. It supports finding a possible need for discussion, rather than full diagnosis or proven intervention. Trainer creation authority conflicts with the stated reservation and needs an explicit decision.
21 September: explain unsafe lifting shortcuts and verify released stored energy before equipment inspection	A lifting posture choice retains correction; isolation uses stop, lock, try-start verification and controlled restart	Posture feedback explains a simplified correction, but the task does not assess weight limits or every lifting factor. Isolation has no separate residual-energy check. These simplifications require qualified review rather than a claim of complete procedural coverage.
21 September: simpler controls on smaller screens	Named actions complement scene targets; instruction/action panel stacks beneath the scene on phones	Directly addresses difficult touch selection. Most steps expose one action, limiting independent choice; touch and keyboard execution remain different evidence from source layout.

Dated request and initial problem	Current design response	Evaluation and remaining action
28 September: understandable errors and an accurate learner-to-trainer record	Separate task feedback, save status, Retry save and scoped history	Same-page retry is supported. Reloading an unsaved completion loses its in-memory save identity while a local completed marker can remain. T25 adds the missing interrupted-page check.

The spill and isolation omissions concern required decisions, not scene appearance. Qualified procedure review must precede a consistent update to definitions, scoring, feedback, guide and checks. These corrections remain proposed.

Saving recovery is also partial: one attempt identifier supports retry while the result remains open, but there is no restored pending submission after leaving or reloading. The guide gives the present workaround; T23 and T25 define the consistency and interruption checks needed for a durable-recovery correction.

How feedback moves through a design change

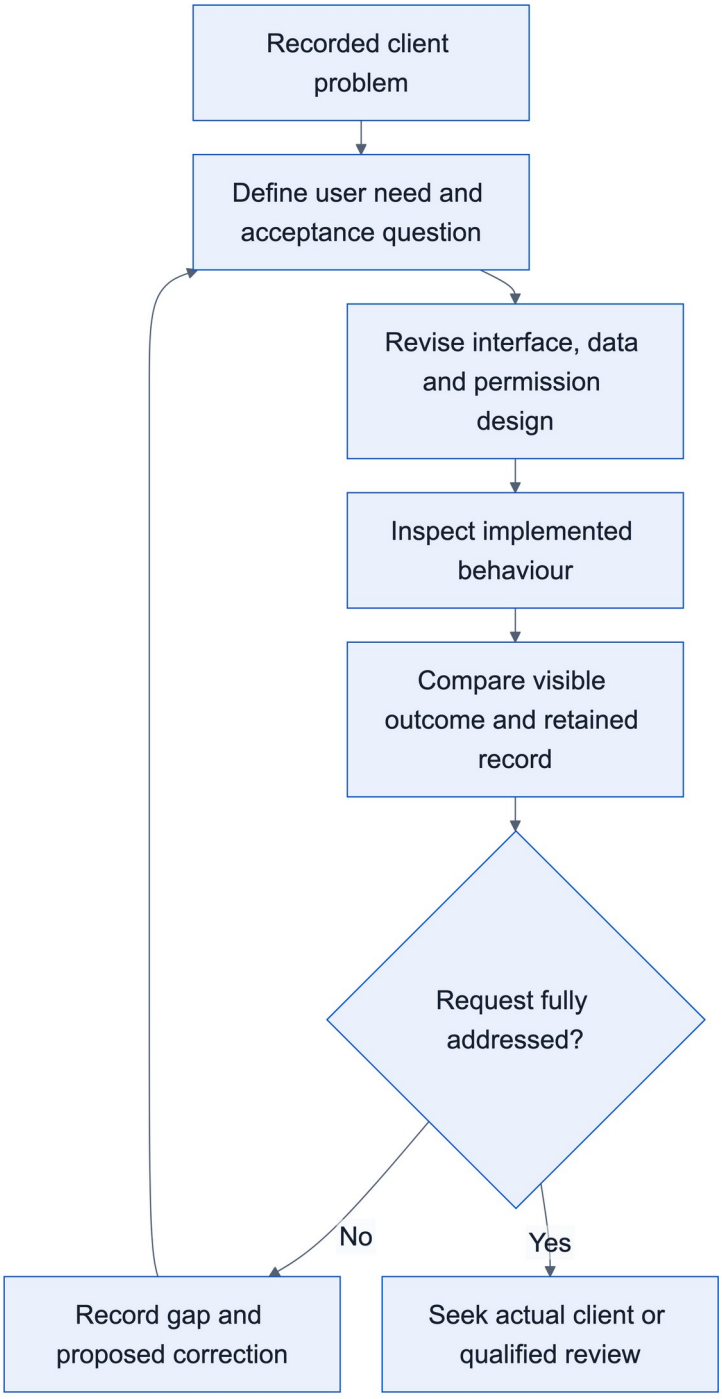


Figure 1 Method for evaluating a feedback response. Arrows describe the review method, not a claim that all changes completed every stage. Actual client acceptance remains separate from implementation and local tests.

3 Weekly development structure

The continuation project plan sets out intended task windows, dependencies, responsibilities and review conditions. The outcomes below provide the separate progress review.

The original roadmap groups Weeks 8 and 9 as Curriculum and Supervision, Weeks 10 and 11 as Integration and Enterprise Testing, and Week 12 as Handover. The entries below identify the main focus within those stages. Learner, management, UI and 3D work overlap; modelling and interaction refinement continue across the later development period rather than being confined to Week 10.

The continuation schedule introduces the 3D proposal on 7 September, within Week 8. Starting with one task gives modelling, equipment animation and controls time to develop alongside the learner route. The later emphasis on 3D integration in Week 10 therefore concerns bringing that continuing work together, rather than starting and finishing the whole scene in one week.

Table 3 Later weekly workstreams

Week	Documentation period	Workstream	Connection to the plan
8	7 to 13 September 2026	Learner reliability and feedback	Curriculum and supervision phase: refine the learner foundation.
9	14 to 20 September 2026	Management and learning records	Curriculum and supervision phase: develop reporting and completion visibility.
10	21 to 27 September 2026	3D integration and task refinement	Integration and enterprise testing phase: connect practical tasks to the learner route.
11	28 September to 4 October 2026	Integration and verification	Integrate and test the enterprise extensions.
12	5 to 9 October 2026	Handover and demonstration preparation	Prepare the final product presentation and technical documentation.

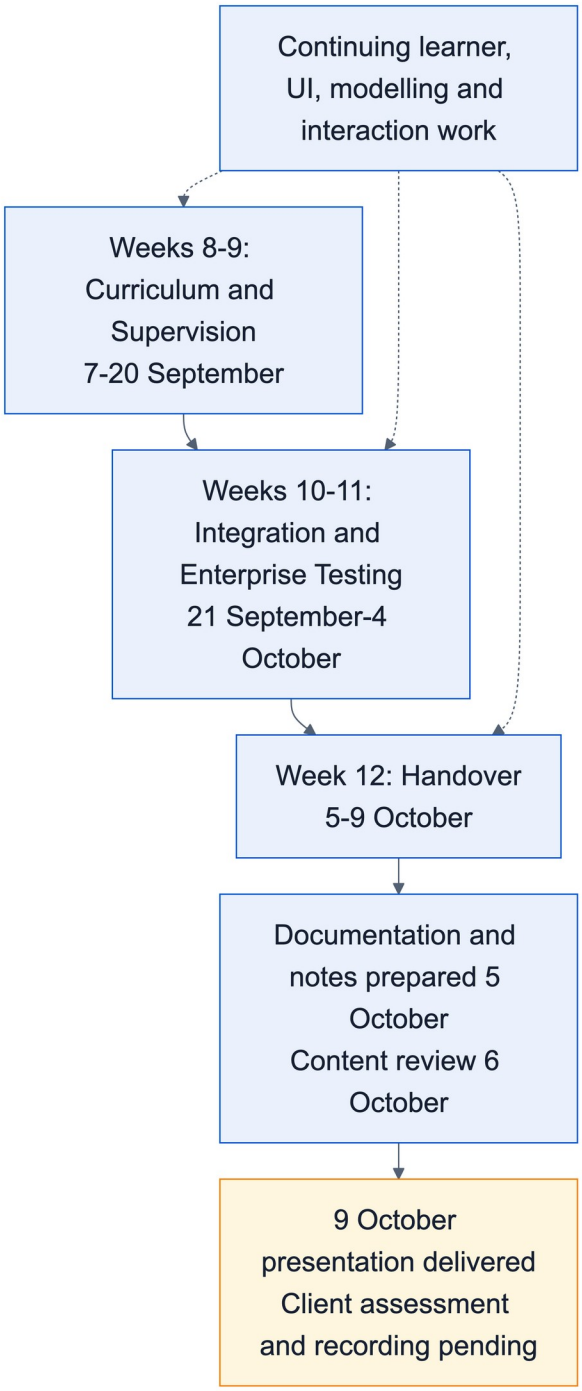


Figure 2 Original later-stage sequence with overlapping development. Week periods include weekends; the final documentation period ends on 9 October. The 5 and 6 October entries identify completed documentation activity. The final box preserves the earlier pending-feedback status; the supplied signed feedback is now retained in B3 Appendix 07.

Week 8 Learner reliability and feedback

Development focus: Lesson instructions, activity feedback, saving states, progress meaning and assessment recovery, alongside initial task planning and continuing 3D modelling and interaction work.

Rijan: persistence, result state and technical task design. Sushank: lesson layout, labels and feedback presentation.

Outcome and evaluation: separate loading, correctness and saving feedback make the learner's next action clearer. A valid result can remain available when its review refresh fails. This addresses the client's completion concern at both the interface and persistence layers. The remaining question is

whether a learner can interpret those states independently; code and a prepared route establish different evidence from observed understanding.

Week 9 Management and learning records

Development focus: Administrator and trainer workflows, assignment boundaries, consolidated records and analytics, alongside continuing practical-task and UI development.

Rijan: account routes, permissions, assignments and record calculations. Sushank: management navigation, directory, filters and responsive forms.

Outcome and evaluation: trainer records make the learner's history inspectable within a current assignment. Administrators have wider management permissions. Keeping history with the learner allows responsibility to change without rebuilding that history. The extension is useful only if direct requests obey the same boundary as the directory and if totals distinguish lessons, assessments, practice and certificate holders.

Week 10 3D integration and task refinement

Development focus: Integration of warehouse models, five quest task spaces, learning steps, camera views and animation with instructions and practice outcomes.

Rijan: Three.js models, quest logic, motion and interaction integration. Sushank: task layout, labels, visual hierarchy and phone controls.

Outcome and evaluation: dedicated spaces connect the model, target, accepted action and explanation. The five tasks give the continuing asset work a practical learner purpose. Geometry, cameras and motion still need to agree with task state and phone controls. Visual detail is therefore one part of integration quality; it cannot establish that the sequence or saved result is correct.

Week 11 Integration and verification

Development focus: Practice recording, assessment/certificate boundaries, session recovery, responsive integration and regression checks.

Rijan: server recording, scoring, security and technical checks. Sushank: interface consistency, responsive review and presentation visuals.

Outcome and evaluation: practice decisions reach server records, chapter and course outcomes remain distinct, and account changes clear prior private state. The earlier retained development record reports 411 tests and local database/browser verification. Application of migration 081 to the hosted database was pending in that record; the later main release record reports its application on 7 October in Week 12. The 5 October selection is also recorded under Week 12. Those later dates must not be moved into Week 11.

Week 12 Handover and demonstration preparation

Development focus: consolidate the design reports, setup instructions, slide outline and release review. The initial application source copy was prepared on 5 October and reconciled on 6 October; later submission revisions and checks are recorded separately below.

Rijan: technical explanation and demonstration operation. Sushank: interface explanation and visual preparation. The presentation plan assigns rehearsal, questions and follow-up to both.

Outcome and evaluation: the source copy, design reports, user guidance, session plan and separate speaking script provide an **inspectable handover**. The 5 October test record adds selected local execution evidence; the 6 October review clarifies record semantics and presentation preparation.

The main application's **7 October release record** reports 423 tests in 74 files, migration 081 applied to the hosted database, production configuration and a bounded authenticated smoke check. It supersedes the earlier pending-migration status for that release, while the retained package's source identity and additional failure cases remain separate.

Communication and final-preparation dates

Presentation delivery on 9 October is confirmed. Rehearsal completion, the actual question exchange and administrative handover require their own records. Section 6 distinguishes the development outcome from those remaining checks.

Rijan leads technical setup and operation; Sushank leads presentation visuals, interface explanation and client correspondence. The presentation plan assigns explanation and questions to both members.

4 Plan comparison and scope response

How the later work develops the prototype

The learner's saved outcome is the dependency linking curriculum, supervision and integration. Clear instructions and feedback help the learner complete an action; the trainer then needs a permitted record with the same meaning. Guided tasks add another link: their accepted steps and correction history must agree with the recorded practice outcome. The plan is most useful when evaluated through those dependencies.

The 3D work continued alongside learner and management development because a scene's models, movement and controls need refinement together. A finished asset can still require changes to its camera or instruction. This explains overlapping workstreams within the existing stages. The team's daily activity supports the sustained effort described, while the available records do not establish exact hours or individual feature-delivery dates.

Table 4 Planned work compared with current outcomes

Original later-phase plan	Current outcome	Variance or remaining work	Response and responsibility
Curriculum expansion and supervision	Management, records and analytics are present alongside the learner route	Broader content approval is not established	Both retain the focused learner demonstration; qualified review is needed for wider content
Enterprise integration and testing	Earlier local results and the separate 7 October main release record are available	Exact source-to-release match, unresolved failure cases and wider learner evaluation remain	Rijan leads technical verification; Sushank reviews the visible status and recovery
SCORM or xAPI exploration	No implemented LMS exchange is established	Interoperability remains outside the demonstrated outcome	Discuss its client value before expanding scope; no delivered exchange is claimed
User evaluation with logistics workers	No completed participant study is supplied	Independent learner interpretation and workplace suitability remain unmeasured	Plan learner observation and qualified content review with an appropriate reviewer

The responsibility column describes the response needed for remaining work. It does not imply that an evaluation session, content approval or interoperability agreement has already occurred.

Dependencies between technical and interface work

Dividing the project into technical and visual tasks did not remove the need to work together. A saving problem, for example, involves both the record Rijan retains and the message Sushank presents. The message needs to tell the learner what happened and what they can do next. That gave us a more useful way to judge a task than checking whether each member's part worked separately.

Table 5 Technical and interface dependencies

Connected work	Technical responsibility	Interface responsibility	Shared review question
Learning and saving	Retain the selected account/result and reject stale responses	Explain Saving, Saved, Failed and Retry	Does the learner know which operation succeeded?
Guided task	Match accepted decisions, motion and server outcome	Keep instruction, target and controls readable	Does the visible step agree with the accepted action and retained history?
Trainer records	Resolve assignment and calculate permitted records	Present categories, empty/unavailable states and filters	Is the record both authorised and understandable?
Handover	Identify source, schema and release limitations	Assemble readable captures and explain the route	Can both members operate and explain the same selected environment?

5 Evaluation of scope and outstanding work

Judging whether feedback changed the design

The progress response has evidence at the calculation boundary. In the 6 October fixture, duplicate records, an activity and a removed lesson leave one completed current lesson out of two: 50%, with the assessment still Not attempted. This supports the separation the client requested and explains why counting every progress row would mislead. Independent interpretation of the displayed categories remains the next usability check.

The supervision extension has a similar trade-off. Assigned records give the client a way to identify incomplete learning without displaying the entire workforce to every trainer. Wider account operations increase responsibility and verification work. The unresolved trainer-provisioning permission should therefore be confirmed separately from the usefulness of reporting. If the client rejects that permission, the requirement and server route need revision; changing the button alone would leave the underlying authority intact.

The 6 October lifting fixture similarly supports the corrective-practice design: carton → stoop → squat → shelf derives 100% completion and one retry, despite the supplied browser score of zero. That is recorded calculation evidence; it does not verify the saved row or trainer display. The current trainer summary exposes completion and retries rather than every choice. It can identify a need for discussion, while diagnosis of the particular shortcut requires the learner's account or a future permitted detail view.

The extension's value depends on maintaining those connections through saving, assignment checks and understandable records. The test plan's evidence table shows which boundaries have recorded support and which still need integration or observation. Qualified content review and worker evaluation remain necessary before claiming transfer to workplace performance.

Taken together, these examples show **progress in record meaning** rather than proof of a finished training service. The calculation fixtures support counting distinct current lessons and retaining correction within formative practice. They do not establish that a learner understands the labels or a trainer can choose appropriate support.

The next evaluation should follow the same outcome through calculation, persistence and **independent interpretation**. If the stored result is correct but its explanation is misunderstood, the response needs a wording or interaction change; if the response disagrees with the row, it needs a recording correction. This distinguishes useful next work from simply adding more assertions or screens.

We had considered 3D early, but its time and scope were difficult to judge for a two-person project. **Backend foundations took priority** for the first prototype. Later exploration made a practical extension worth pursuing, especially when the client supplied situations the tasks could address.

That did not make every extra model or animation necessary. The useful question became whether the learner could understand the task, complete it and find an accurate record afterwards. **Finishing that whole route** should come before enlarging the scene or asset set.

What changed in how we worked

The 3D direction and early development were shared. **Rijan led the later Three.js implementation and integration**, and **Sushank led the UI and responsive layouts**. Both reviewed how tasks, controls and records should connect.

Rijan found collaboration difficult at first and learned to separate responsibilities into bounded tasks that the other person could understand. That experience is relevant to the later integration work. A request such as “make progress clearer” leaves too much for the person receiving it to interpret. The client's example gave us a better starting point: distinguish reading, passed questions and completed learning. From there, we could explain the result the learner needed to see and the records needed to support it.

The branding work taught a related lesson. Both members refined the logo, fonts and colours after the initial monogram direction proved unsatisfactory. Shared work therefore involved questioning an earlier choice, rather than just dividing a finished idea into jobs. The same approach matters when reviewing a practice task: one member may see a working sequence while the other notices that the instruction or next action is unclear. We need both views to judge the result.

Looking back, the project became more demanding when we had to connect the parts we could already build. A lesson, scene and trainer screen can each work on their own while disagreeing about what the learner has completed. The progress and recovery issues made that connection visible. The main lesson for our next project is to define what a complete user action means before dividing the work, then review its screen, saved record and recovery together.

The main shortfall against the wider plan is that worker evaluation and LMS exchange are not completed outcomes. The application has gained depth in its own learner and supervision route, while workplace suitability and interoperability remain unresolved. The next scope discussion should establish their value to the client. That would support a reasoned priority decision instead of treating every original ambition as an equally urgent feature.

For further handover, permissions, scoring, saved records and the selected deployment target take priority over secondary demonstrations. The presentation plan allocates question time and a fallback; the requirements and test mapping identifies behaviours needing verification. Recorded rehearsal and client-response evidence are still required to judge how that preparation worked in the delivered session.

Evaluating the quality of the response

The following observations test whether the implemented response resolves the client's underlying problem.

Table 6 Evaluating the response to feedback

Development response	What it improves	Remaining weakness and next observation
Separate progress, assessment and practice categories	Makes the meaning of completion more explicit	Ask a learner and trainer to explain an example record without team assistance
Explanations accompanying guided choices	Connects an action to its procedural reason	Ask a qualified reviewer to identify misleading or incomplete instructions before wider use
Saved-result and failed-review recovery states	Helps preserve completed work when a later request fails	Observe whether a learner retries the failed operation without replaying or resubmitting

These proposed observations would close a specific evaluation gap: current evidence shows how the response is designed, while independent interpretation would show whether it resolves the client's concern. Qualified procedure review must still establish whether the underlying content is suitable.

6 Final milestone and verification

The 5 October selection passed 48 tests in nine files against the earlier 358-file snapshot. Mocked checks cover selected progress, permission, scoring, request and session behaviour; they do not establish hosted migration 081.

The 6 October selection passed 67 tests in fourteen files against the reconciled 365-file snapshot, including generated credentials and required password change. These overlapping selections do not date feature delivery. The configured password-change journey and failed new-session recovery still need browser checks.

Completion at the project cutoff

The continuation period is 7 September–9 October, and the final presentation took place on **9 October**. The earlier local selections and separate 7 October release record support their stated checks. They do not establish an exact demonstrated-version match, a completed learner study or final technical acceptance.

The supplied signed feedback recognises the connected route and identifies further development priorities. Its signing date is not shown. Exact session evidence and confirmed administrative handover remain separate.

Priorities for proposed corrections

The remaining work should follow consequences and dependencies. Procedural omissions and permission disagreements need a content or client decision before implementation; recovery defects need a consistent record contract before additional visual refinement. The priorities below propose how to address those issues; their owners and dates still need agreement.

Table 7 Proposed corrections and evidence of completion

Priority and issue	Decision or dependency	Connected design change	Evidence needed to close it
Before workplace use: omitted spill/PPE and residual-energy decisions	Qualified reviewer confirms organisation-specific content	Update task instructions, required choices, feedback, scene and server scoring together	Reviewed procedure and consistent task/guide definitions; T12/T26 compatibility and observed interpretation

Priority and issue	Decision or dependency	Connected design change	Evidence needed to close it
Before approving management scope: trainer learner creation	Client explicitly accepts or rejects the narrower permission	If rejected, revise server authority, interface, guide and role model	Recorded scope decision plus permitted/denied account tests; a hidden button alone is insufficient
Before calling practice recovery dependable: conflicts and lost pending saves	Define the relationship between the attempt, owner, payload and retained outcome	Return a consistent existing result on retry; propose account-bound pending-save recovery across interruption	T23 and T25 response/row comparisons, including an already saved attempt after a lost acknowledgement
Before relying on account-creation recovery: failed assignment and compensation	Establish the actual account and assignment state before another creation attempt	Check the compensating deletion result and explain an account left behind accurately; retain profile/assignment partial-success guidance	T24 creation, failed-compensation and checked-retry observations in the selected environment
Before treating accepted requests as persistable: layered data bounds	Agree compatible request, action and database limits	Detect non-retryable input/storage failures clearly and preserve the pending result for support	T19 boundary results at each layer and an accurate user-facing recovery instruction
Before revising task steps: historical compatibility	Establish a task version/ID and old-progress policy	Preserve original saved outcomes; make a changed definition's restart or migration explicit	T26 old/new fixtures and retained original row; reconstructed actions are not recorded learner choices

Rijan's system and integration responsibility and Sushank's interface responsibility provide complementary review areas for such corrections. The procedural reviewer and client decide content and organisational authority; the team cannot settle those decisions through implementation alone.
