SARAS Continuation Project Plan — Weeks 8–12

Module: CET257 Enterprise Project
Team: Team 9 — SARAS Labs
Members: Rijan Kapur Poudel and Sushank Jung Rawal
Client: Mr. Ninson Lama, Autoport Pvt. Ltd.
Planning period: 7 September–9 October 2026
Purpose: Retain the intended schedule, responsibilities and review conditions for Weeks 8–12.

Plan reference date: 7 October 2026

1 Purpose and planning approach

This document retains the **original intended schedule**. Its future tense describes the plan, not the status at submission. The accompanying development review records the current outcomes, including confirmed presentation delivery on 9 October, supplied signed client feedback and outstanding recording and selected release checks. **Planned windows have not been rewritten as completed history**.

This schedule develops the Phase 2 roadmap in the original master project plan, section 8. It sets out planned work, responsibilities, dependencies and review conditions for the period after the Week 7 prototype milestone. Actual progress and changes are recorded separately in the development review.

The work will follow three stages: Curriculum and Supervision in Weeks 8–9; Integration and Enterprise Testing in Weeks 10–11; and Handover in Week 12. Learner improvements, management functions, 3D development and UI work will overlap. The 3D work will begin in Week 8 because modelling, movement, task controls and instructions require continued development and review.

The team will prioritise the client's recorded requests for clearer progress, completion information and consistent explanatory feedback. The existing learner journey will remain the foundation. Management features and guided practice will extend that journey without presenting digital completion as proof of workplace competence.

2 Weekly stage schedule

Table 1 Planned weekly stages and milestones

Week	Start	End	Stage and main focus	Intended milestone
8	Monday 7 September	Sunday 13 September	Curriculum and Supervision: learner reliability, explanatory feedback and initial guided 3D task design	Agree the first-task scope and review the learner improvement priorities
9	Monday 14 September	Sunday 20 September	Curriculum and Supervision: trainer records, management permissions and continuing 3D/UI development	Review the supervision design and an initial connected task route
10	Monday 21 September	Sunday 27 September	Integration and Enterprise Testing: connect guided tasks, learner outcomes and management views	Review the integrated learner-to-practice route and identify defects

Week	Start	End	Stage and main focus	Intended milestone
11	Monday 28 September	Sunday 4 October	Integration and Enterprise Testing: verify access, recording, scoring, recovery and responsive behaviour	Review release risks, the demonstration scope and draft supporting documents
12	Monday 5 October	Friday 9 October	Handover: complete reports, guides, source selection, presentation preparation and final review	Finish documentation and final checks by 9 October

All dates in the tables are in 2026. The task dates are planned windows and checkpoints, rather than statements of actual completion or evidence that a client exchange took place.

3 Planned work packages

Week 8 — 7–13 September: learner foundation and early 3D work

Table 2 Week 8 planned work packages

Task	Planned dates	Work to undertake	Responsibility	Dependency and intended output
W8-01	7 September	Review the Week 7 feedback and prioritise progress, completion and explanation improvements	Both; Rijan coordinates	Retained client response → prioritised learner backlog
W8-02	7–9 September	Refine the learner requirements, progress meanings, saving states and recovery conditions	Rijan: persistence and system behaviour; Sushank: wording and layout	W8-01 → updated user stories and acceptance conditions
W8-03	7–13 September	Propose one manageable workplace task; begin scene layout, models, controls and instruction design	Rijan: technical task and models; Sushank: instructions and interaction layout	First-task scope → initial 3D task design and assets
W8-04	10–13 September	Develop learner improvements and review feedback, saved state and phone/keyboard interaction together	Both within their technical/UI responsibilities	W8-02 → learner route ready for further integration checks
W8-05	13 September	Review the week's intended outputs, note unresolved issues and prepare the next work priorities	Both	W8-02–04 → progress record, risks and Week 9 priorities

The first client communication topic is planned for **7 September**: ask which workplace situation should guide the first practical task. The team will retain the actual message and response if the exchange occurs; development will not depend on an assumed reply.

Week 9 — 14–20 September: supervision and continuing task development

Table 3 Week 9 planned work packages

Task	Planned dates	Work to undertake	Responsibility	Dependency and intended output
W9-01	14–16 September	Define administrator and trainer permissions, learner assignments and the information each role should see	Rijan: access/data design; Sushank: navigation and record layout	W8 learner requirements → permission matrix and management flows
W9-02	14–20 September	Continue modelling, movement, camera views and task controls alongside readable instructions	Rijan: scene and interaction logic; Sushank: task interface and phone controls	W8-03 → initial interactive task route
W9-03	17–20 September	Develop assignment handling, trainer records and clearly defined progress/completion summaries	Rijan: permissions and calculations; Sushank: forms, records and visual summaries	W9-01 → supervision prototype and record definitions
W9-04	20 September	Review learner, management and task interfaces together; identify integration dependencies	Both	W9-02–03 → agreed integration priorities and open checks

The communication topic planned for **14 September** concerns trainer information and learner assignments. Broader management requirements will remain subject to review rather than being described as client-approved procedures.

Week 10 — 21–27 September: integration of practical tasks and records

Table 4 Week 10 planned work packages

Task	Planned dates	Work to undertake	Responsibility	Dependency and intended output
W10-01	21–24 September	Connect the continuing 3D models, movement, accepted actions and explanations into guided task sequences	Rijan: task-state integration; Sushank: controls and visible feedback	W9-02 → guided practice route
W10-02	21–27 September	Refine learning steps, camera positions, labels, navigation and responsive layouts	Sushank leads UI review; Rijan supports behaviour changes	Learner and task routes → consistent desktop/phone experience
W10-03	24–27 September	Connect practice outcomes to saved learner records and permitted trainer views	Rijan: recording and access; Sushank: outcome/record presentation	W9-03 and W10-01 → connected learner-to-practice-to-trainer route
W10-04	27 September	Walk through the integrated route and record defects, unclear instructions and unresolved requirements	Both	W10-01–03 → integration issue list and Week 11 verification priorities

The communication topic planned for **21 September** is the relevance of the selected tasks and their explanations. Additional task scope will depend on the first route being understandable and maintainable; the schedule does not require every model to be built within Week 10.

Week 11 — 28 September–4 October: verification and documentation drafts

Table 5 Week 11 planned work packages

Task	Planned dates	Work to undertake	Responsibility	Dependency and intended output
W11-01	28 September–2 October	Check scoring boundaries, permitted/denied requests, practice recording, retry behaviour and session recovery	Rijan leads technical checks; Sushank checks visible results	Integrated routes → retained test results and defect records
W11-02	28 September–4 October	Review responsive behaviour, keyboard operation, feedback consistency and failed-save recovery	Sushank leads interface checks; Rijan supports fixes	W10 routes → usability/accessibility findings and corrections
W11-03	28 September–4 October	Prepare Assignment 2 user/system design, testing documentation, user guides and client/security evaluations	Rijan: technical/report coordination; Sushank: interface explanation and figures; both review	Requirements, design and actual results → B1, B3 and B4 drafts
W11-04	28 September–4 October	Review the available promotional material against the identity, links and submission specifications; record any files still awaited	Website: both; poster/visual review: Sushank	Available promotional artefacts → B2/B7 review notes and outstanding items
W11-05	4 October	Review outstanding release risks, draft documents, demonstration scope and evidence for individual reflection	Both	W11-01–04 → handover priorities and a bounded demonstration route

The communication topic planned for **28 September** is the client's final-review priorities. End-to-end evaluation will require an appropriate participant and actual retained observations. If access is unavailable, the team will record that limitation rather than treating a walkthrough as a completed user study. LMS exchange exploration from the original roadmap will remain secondary to reliable core behaviour and will not be described as delivered integration without an implemented exchange.

Week 12 — 5–9 October: final documentation and demonstration preparation

Table 6 Week 12 planned work packages

Task	Planned dates	Work to undertake	Responsibility	Dependency and intended output
W12-01	5 October	Consolidate design reports, user/operation guidance, selected application source and presentation content	Rijan: technical/source coordination; Sushank: interface explanation and visuals; both review	Week 11 drafts → coherent handover material

Task	Planned dates	Work to undertake	Responsibility	Dependency and intended output
W12-02	6 October	Check document/source consistency and prepare the final-session invitation	Both; Rijan coordinates client contact	W12-01 → reviewed documents and invitation draft; actual confirmation to be retained
W12-03	7 October	Assemble presentation material, select demonstration evidence and hold the self/peer contribution discussion	Rijan: technical route; Sushank: presentation visuals; both assess contributions	Verified contribution evidence → presentation preparation and accurately completed B5 forms when agreed
W12-04	8 October	Check the selected demonstration environment and rehearse the twenty-minute session, including fallback and questions	Rijan: environment/operator checks; Sushank: interface/visual checks; both rehearse	Selected source, configuration and presentation → actual readiness results and timed rehearsal notes
W12-05	9 October	Deliver the planned client presentation if confirmed; record actual feedback, actions and remaining limitations	Both	W12-04 and client availability → session record and feedback form after delivery
W12-06	7–9 October	Complete the personal evaluation, twelve-week blog and twelve separate reflections; check supporting evidence and links	Rijan for his Assignment 3 portfolio; Sushank supplies relevant shared-work evidence	Actual contribution and outcomes → checked personal portfolio content
W12-07	9 October	Complete final content checks across B1–B7 and Assignment 3; fix inconsistencies and identify any unresolved submission item	Both for Assignment 2; Rijan for his Assignment 3	W12-01–06 → documentation complete within the cutoff

Handover status: the 9 October presentation was delivered. The session plan remains a preparation record; measured timing, the exact delivered copy and confirmed administrative handover need separate evidence. B3 Session Records documents the presentation outcome.

4 Workstream overlap

Table 7 Planned overlap between workstreams

Workstream	Week 8	Week 9	Week 10	Week 11	Week 12
Learner progress and feedback	Requirements and refinement	Continue refinement	Integrate with practice	Verify recovery and result meaning	Final checks and explanation
Guided 3D practice	First-task scope and assets	Models, movement and controls	Guided-task integration	Refinement and verification	Demonstration and operation guidance

Workstream	Week 8	Week 9	Week 10	Week 11	Week 12
Management and records	Identify supervision needs	Permissions and records	Connect saved outcomes	Verify scope and calculations	Demonstrate permitted records
UI and responsive behaviour	Learner/task layouts	Management/ task controls	Shared route refinement	Keyboard/phone review	Presentation and user guidance
Documentation and evidence	Requirements and planning	Flows and record definitions	Update design/test coverage	Report and guide drafts	Complete by 9 October

Tasks in different workstreams may run together. The dependencies identify which output needs to be available before the next connected check, rather than requiring all technical work to finish before UI development starts.

Each milestone will be judged against the inspectable output in its work package. An initial scene can support a control review without being a saved practice route; an account screen can support layout review without establishing assignment isolation. At integration, both the visible outcome and its record will need to be checked together. This allows work to overlap while keeping partial outputs distinct from the complete learner-to-trainer journey.

5 Responsibilities and review conditions

Rijan will coordinate the schedule, system logic, database, authentication, technical integration, technical documentation and demonstration operation. Sushank will lead frontend/UI work, layout, visual design, responsive interfaces and presentation visuals. Both will contribute to UI decisions, review connected behaviour, discuss priorities and answer client questions. These functional responsibilities do not assign contribution percentages or claim exclusive authorship of shared work.

The planned review dates are **13, 20 and 27 September**, **4 October**, and the final content check on **9 October**. Each review will compare intended outputs with the available work and distinguish **completed, partly completed and unverified behaviour**.

The team will identify the dependency preventing the next milestone, assign the next action and record what observation would show it is resolved. Changes will identify the requirement affected, the reason, the responsible person and the effect on the remaining schedule.

A changed scope or date will remain distinct from the original planned window; **scheduling a review does not establish that it occurred**.

Table 8 Risks, dependencies and review conditions

Risk or dependency	Planned response	Condition for the next stage
3D modelling and interaction take longer than expected	Begin in Week 8, develop one manageable route first and defer optional detail	Instructions, controls and task-state behaviour can be reviewed together

Risk or dependency	Planned response	Condition for the next stage
Client response or final-session confirmation is delayed	Ask focused questions and retain unresolved decisions; prepare a bounded demonstration	Use actual confirmation and record only feedback received
Saved records, scoring or role restrictions are unreliable	Prioritise affected checks before presentation polish; retain failures and limits	Demonstration claims agree with actual recorded behaviour
Source and selected environment differ	Check source, schema and configuration together; prepare a clearly identified fallback	The demonstrated environment and its limitations are known
Documentation or evidence is incomplete near the cutoff	Draft during Week 11 and use 5–9 October for consolidation and final checks	Content, links and missing items are reviewed by 9 October

The content cutoff remains **9 October**. Submission preparation and administrative delivery follow the completed development account. Check the official Canvas instructions and deadline before uploading; no independently verified university deadline is recorded here. These arrangements do not add another development week or extend the weekly documentation beyond 9 October.

7 Dependencies controlling the planned handover

The original plan allowed 3D and interface work to overlap. Integration depended on both routes being ready; adding more scene detail alone could not complete the learner-to-trainer journey. The diagram summarises dependencies already identified in the work packages and does not turn planned dates into actual completion dates.

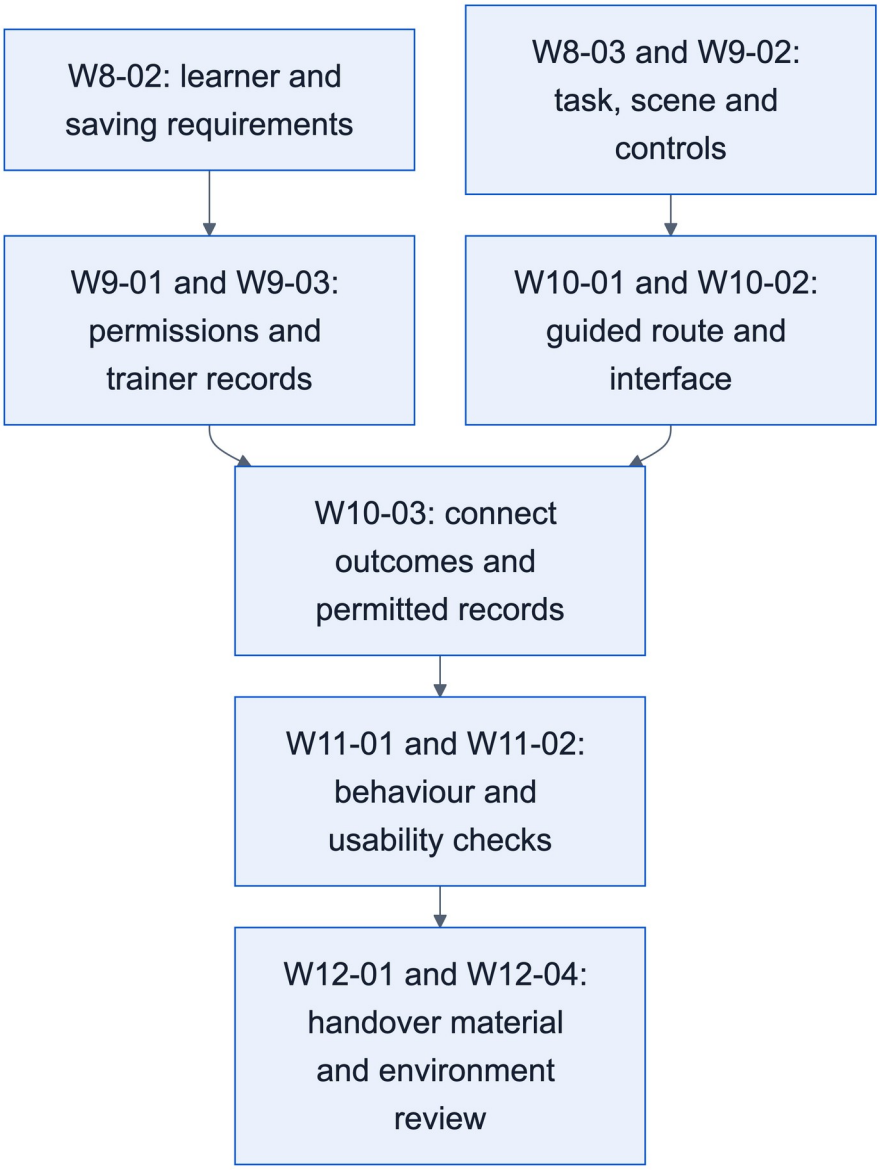


Figure 1 Planned dependencies. Supervision and 3D/interface work converge before verification and handover.

If a permission or saved-record check remains open, the response is to bound the demonstration and retain the unresolved release condition. If an interface explanation is unclear, revise the instruction and repeat the relevant user task. This protects the critical route while retaining optional content expansion as a separate decision. Actual outcomes and remaining checks are recorded in the development review and testing plan.

8 Related project documents

Section 8 of the original master plan supplies the planned stages, while the development review evaluates actual outcomes. The testing plan defines acceptance conditions, the later communication record covers review topics, and the presentation plan describes the prepared demonstration route. The weekly blog evaluates individual contribution and learning.
